
D	0	Task Mode	Task Name					Duration	Start	Finish
1		**	Planni	ing						
2	V	*		decide on Project S	Subject			1 day	Thu 5/19/22	Thu 5/19/22
3	✓	*	Online S	Search				4 days	Thu 5/19/22	Tue 5/24/22
4	✓	*	Literatu	re Review				2 days	Tue 5/24/22	Wed 5/25/2
8	V	*	Project 1	Brief				4 days	Thu 5/26/22	Tue 5/31/22
10	✓	*	Stakeho	lder sign off of Pl	anning Phase			1 day	Wed 6/1/22	Wed 6/1/22
11		**?	Design	1						
12	✓	*	Paper D	emo				5 days	Wed 5/25/22	Tue 5/31/22
15	✓	*	Project S	Spec				5 days	Wed 5/25/22	Tue 5/31/22
19	~	*	Charts a	and Network				4 days	Wed 6/1/22	Sat 6/4/22
24	~	*	Stakeho	lder sign off of D	esign Phase			1 day	Mon 6/6/22	Mon 6/6/22
25		*?	Execu	tion and Moi	nitoring & Co	ntrol				
26	✓	*	Impleme	entation			8 days	Sun 6/5/22	Tue 6/14/22	
32	✓	*	Enhance	ed Implementatio	n		6 days	Tue 6/14/22	Tue 6/21/22	
39	✓	*	Midtern	n PPT and Presen	tation		3 days	Wed 6/22/22	Fri 6/24/22	
40	✓	*	Return o	of Peer Reviews			8 days	Sat 6/25/22	Tue 7/5/22	
49	~	*	Respons	e to Reviewers co	mments		2 days	Wed 7/6/22	Thu 7/7/22	
51	✓	*	Revise, l	Redo				8 days	Fri 7/8/22	Tue 7/19/22
53	V	*	Testing					8 days	Fri 7/8/22	Tue 7/19/22
59	V	*	Stakeho	lder sign off of Ex	xecution and Mon	itoring & Control	Phases	5 days	Wed 7/13/22	Tue 7/19/22
60		7?	Closu	re						
61	V	*	Results,	Conclusions, Fut	ure Work			14 days	Wed 7/13/22	Sun 7/31/22
65	✓	*	Exit Sur	evey				2 days	Mon 7/25/22	Tue 7/26/22
				Task		Inactive Summary			xternal Tasks	
				Split		Manual Task		E	xternal Milestone	\Diamond
D:			ar dala	Milestone	♦	Duration-only			Deadline	+
-		oup 4 Gar 8/1/22	ntt with est	Summary		Manual Summary Rollup)		Critical	
Date.	141011	0/ 1/22		Project Summary		Manual Summary			Critical Split	
				Inactive Task		Start-only	Е	F	rogress	

Page 1

ID		Task	Task Name	Duration	Start	Finish
	Ð	Mode				
66		*	Written Report, PPT and Presentation	9 days	Wed 7/27/22	Sat 8/6/22
72		*	Return of Peer Reviews (Team)	2 days	Mon 8/8/22	Tue 8/9/22
73		*	Return of Peer Reviews (Individual Assessments)	2 days	Sat 8/6/22	Sun 8/7/22
74		*	Document of opinions on teammates	2 days	Sat 8/6/22	Sun 8/7/22
75		*	Response to Reviewers' Comments	2 days	Sun 8/7/22	Mon 8/8/22
76	<u> </u>	*	Individual recording of responses to reviews	2 days	Sun 8/7/22	Mon 8/8/22
77		*	Contact Hours	1 day	Tue 8/9/22	Tue 8/9/22
78		*	Final Course Letter Grade	1 day	Wed 8/10/22	Wed 8/10/22

External Tasks Task Inactive Summary Split Manual Task External Milestone Duration-only Deadline Milestone Project: Group 4 Gantt with est Summary Manual Summary Rollup Critical Date: Mon 8/1/22 Manual Summary **Project Summary** Critical Split Inactive Task Start-only Е Progress Inactive Milestone Finish-only **Manual Progress**

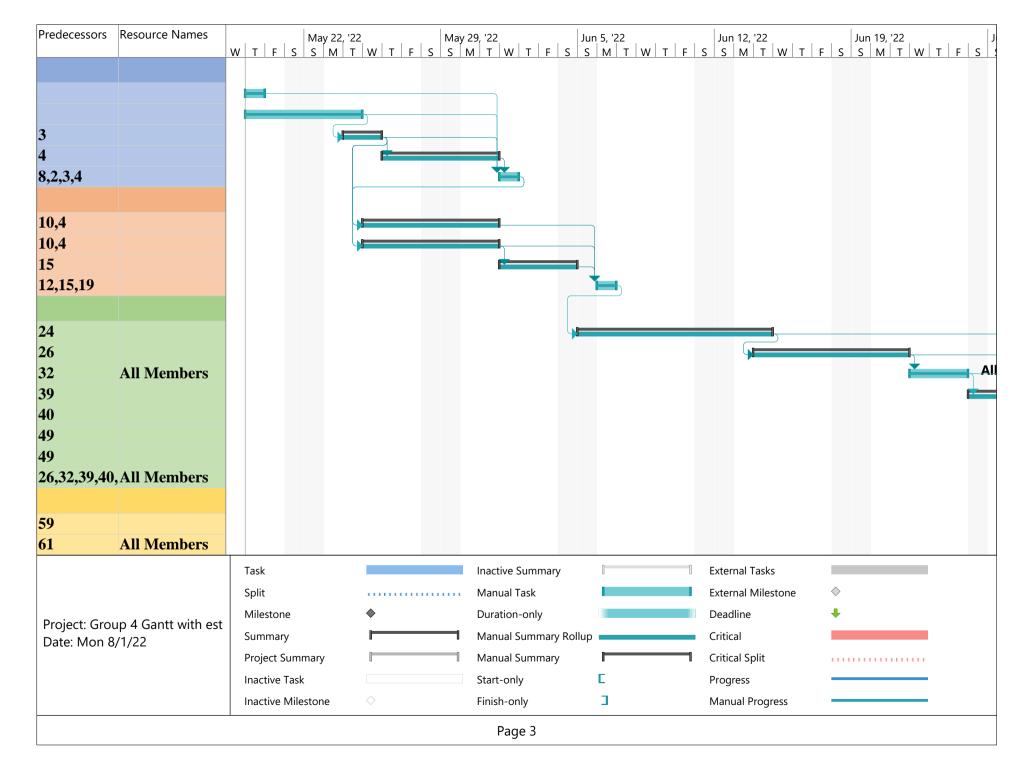

Predecessors	Resource Names				l _N	1av 2	22, '2	2				Mav	v 29,	'22				Ju	ın 5,	, '22					Jun	12,	22					Jun	19,	22			ر
		W	Т	F	s s	5 N	<u>и Т</u>	2 W	Т	F	S	S	M	Т	w	Т	= 9	S	N	<u>и т</u>	W	<u>/ T</u>	F	S	S	M	Т	w	Т	F	S	S	M	T	w T	F	S
65																																					
66																																					
66																																					
	Alex,John,Phil																																				
72,73																																					
	All Members																																				
75																																					
77	N/A																																				

